



DPIC-PO-NEC-299-1002			Classic Schedule Layout						16-Jan-22 12:44													
#	Activity ID	Activity Name	Budgeted Labor Cost	Start	Finish	Original Duration	Schedule % Complete	Performance % Complete	Aug, 2021	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
102	92	NDE Procedure	0.04	22-Nov-21 A	29-Dec-21	21	100%	80%														
103	96	Inspection and Test Procedure for Compressor	0.04	05-Jan-22 A	15-Dec-21	21	47.62%	80%														
104	DPIC-PO-NEC-299-R1-3.1.3 Supply of Material		35.00	14-Nov-21 A	11-Sep-22	301	18.37%	8.78%														
105	DPIC-PO-NEC-299-R1-3.1.3.2 Domestic Supply		10.00	13-Dec-21	27-Mar-22	104	26.28%	0%														
106	DPIC-PO-NEC-299-R1-3.1.3.2.1 Pipe		1.00	24-Jan-22	18-Feb-22	25	0%	0%														
107	141	PO placement (Pipe)	0.10	24-Jan-22	29-Jan-22	5	0%	0%														
108	142	EX Work (Pipe)	0.40	29-Jan-22	13-Feb-22	15	0%	0%														
109	143	Delivery to shop (Pipe)	0.50	13-Feb-22	18-Feb-22	5	0%	0%														
110	DPIC-PO-NEC-299-R1-3.1.3.2.2 Plate		1.00	13-Dec-21	07-Jan-22	25	100%	0%														
111	145	PO placement (Plate)	0.10	13-Dec-21	18-Dec-21	5	100%	0%														
112	146	EX Work (Plate)	0.40	18-Dec-21	02-Jan-22	15	100%	0%														
113	147	Delivery to shop (Plate)	0.50	02-Jan-22	07-Jan-22	5	100%	0%														
114	DPIC-PO-NEC-299-R1-3.1.3.2.3 Flange & Fitting		1.00	13-Dec-21	01-Feb-22	50	37.25%	0%														
115	149	PO placement (Flange & Fitting)	0.10	13-Dec-21	18-Dec-21	5	100%	0%														
116	150	EX Work (Flange & Fitting)	0.40	18-Dec-21	27-Jan-22	40	68.22%	0%														
117	151	Delivery to shop (Flange & Fitting)	0.50	27-Jan-22	01-Feb-22	5	0%	0%														
118	DPIC-PO-NEC-299-R1-3.1.3.2.4 Gasket		1.00	13-Dec-21	22-Jan-22	40	46.33%	0%														
119	153	PO placement (Gasket)	0.10	13-Dec-21	18-Dec-21	5	100%	0%														
120	154	EX Work (Gasket)	0.40	18-Dec-21	17-Jan-22	30	90.87%	0%														
121	155	Delivery to shop (Gasket)	0.50	17-Jan-22	22-Jan-22	5	0%	0%														
122	DPIC-PO-NEC-299-R1-3.1.3.2.5 Bolt & Nut		1.00	13-Dec-21	22-Jan-22	40	46.33%	0%														
123	157	PO placement (Bolt & Nut)	0.10	13-Dec-21	18-Dec-21	5	100%	0%														
124	158	EX Work (Bolt & Nut)	0.40	18-Dec-21	17-Jan-22	30	90.87%	0%														
125	159	Delivery to shop (Bolt & Nut)	0.50	17-Jan-22	22-Jan-22	5	0%	0%														
126	DPIC-PO-NEC-299-R1-3.1.3.2.6 Electrical		1.00	12-Jan-22	21-Feb-22	40	4.5%	0%														
127	161	PO placement (Electrical)	0.10	12-Jan-22	17-Jan-22	5	45%	0%														
128	162	EX Work (Electrical)	0.40	17-Jan-22	16-Feb-22	30	0%	0%														
129	163	Delivery to shop (Electrical)	0.50	16-Feb-22	21-Feb-22	5	0%	0%														
130	DPIC-PO-NEC-299-R1-3.1.3.2.7 Manual valves		1.00	09-Jan-22	17-Feb-22	40	11.33%	0%														
131	165	PO placement (Manual valves)	0.10	09-Jan-22	13-Jan-22	5	100%	0%														
132	166	EX Work (Manual valves)	0.40	14-Jan-22	12-Feb-22	30	3.35%	0%														
133	167	Delivery to shop (Manual valves)	0.50	13-Feb-22	17-Feb-22	5	0%	0%														
134	DPIC-PO-NEC-299-R1-3.1.3.2.8 Instrument		1.00	15-Feb-22	27-Mar-22	40	0%	0%														
135	169	PO placement (Domestic Instrument)	0.10	15-Feb-22	20-Feb-22	5	0%	0%														
136	170	EX Work (Domestic Instrument)	0.40	20-Feb-22	22-Mar-22	30	0%	0%														
137	171	Delivery to shop (Domestic Instrument)	0.50	22-Mar-22	27-Mar-22	5	0%	0%														
138	DPIC-PO-NEC-299-R1-3.1.3.2.9 PLC		1.00	11-Feb-22	23-Mar-22	40	0%	0%														
139	173	PO placement (PLC)	0.10	11-Feb-22	16-Feb-22	5	0%	0%														
140	174	EX Work (PLC)	0.40	16-Feb-22	18-Mar-22	30	0%	0%														
141	175	Delivery to shop (PLC)	0.50	18-Mar-22	23-Mar-22	5	0%	0%														
142	DPIC-PO-NEC-299-R1-3.1.3.2.10 Other material		1.00	04-Jan-22	13-Feb-22	40	17%	0%														
143	177	PO placement (Other material (Domestic) )	0.10	04-Jan-22	09-Jan-22	5	100%	0%														
144	178	EX Work (Other material(Domestic))	0.40	09-Jan-22	08-Feb-22	30	17.5%	0%														
145	179	Delivery to shop (Other material(Domestic))	0.50	08-Feb-22	13-Feb-22	5	0%	0%														
146	DPIC-PO-NEC-299-R1-3.1.3.1 ForeignSupply		25.00	14-Nov-21 A	11-Sep-22	301	15.21%	12.29%														
147	DPIC-PO-NEC-299-R1-3.1.3.1.1 Special Valves		1.70	02-Jan-22	15-Jun-22	165	11%	0%														
148	105	PO placement (Other Valves)	0.17	02-Jan-22	11-Jan-22	10	100%	0%														
149	106	EX Work (Other Valves)	0.68	12-Jan-22	11-May-22	120	2.5%	0%														
150	107	Custom clearance (Other Valves)	0.51	12-May-22	10-Jun-22	30	0%	0%														
151	108	Delivery to shop (Other Valves)	0.34	11-Jun-22	15-Jun-22	5	0%	0%														
152	DPIC-PO-NEC-299-R1-3.1.3.1.2 Instrument		1.70	29-Jan-22	14-May-22	105	0%	0%														
153	110	PO placement (Instrument)	0.17	29-Jan-22	08-Feb-22	10	0%	0%														

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work


Milestone









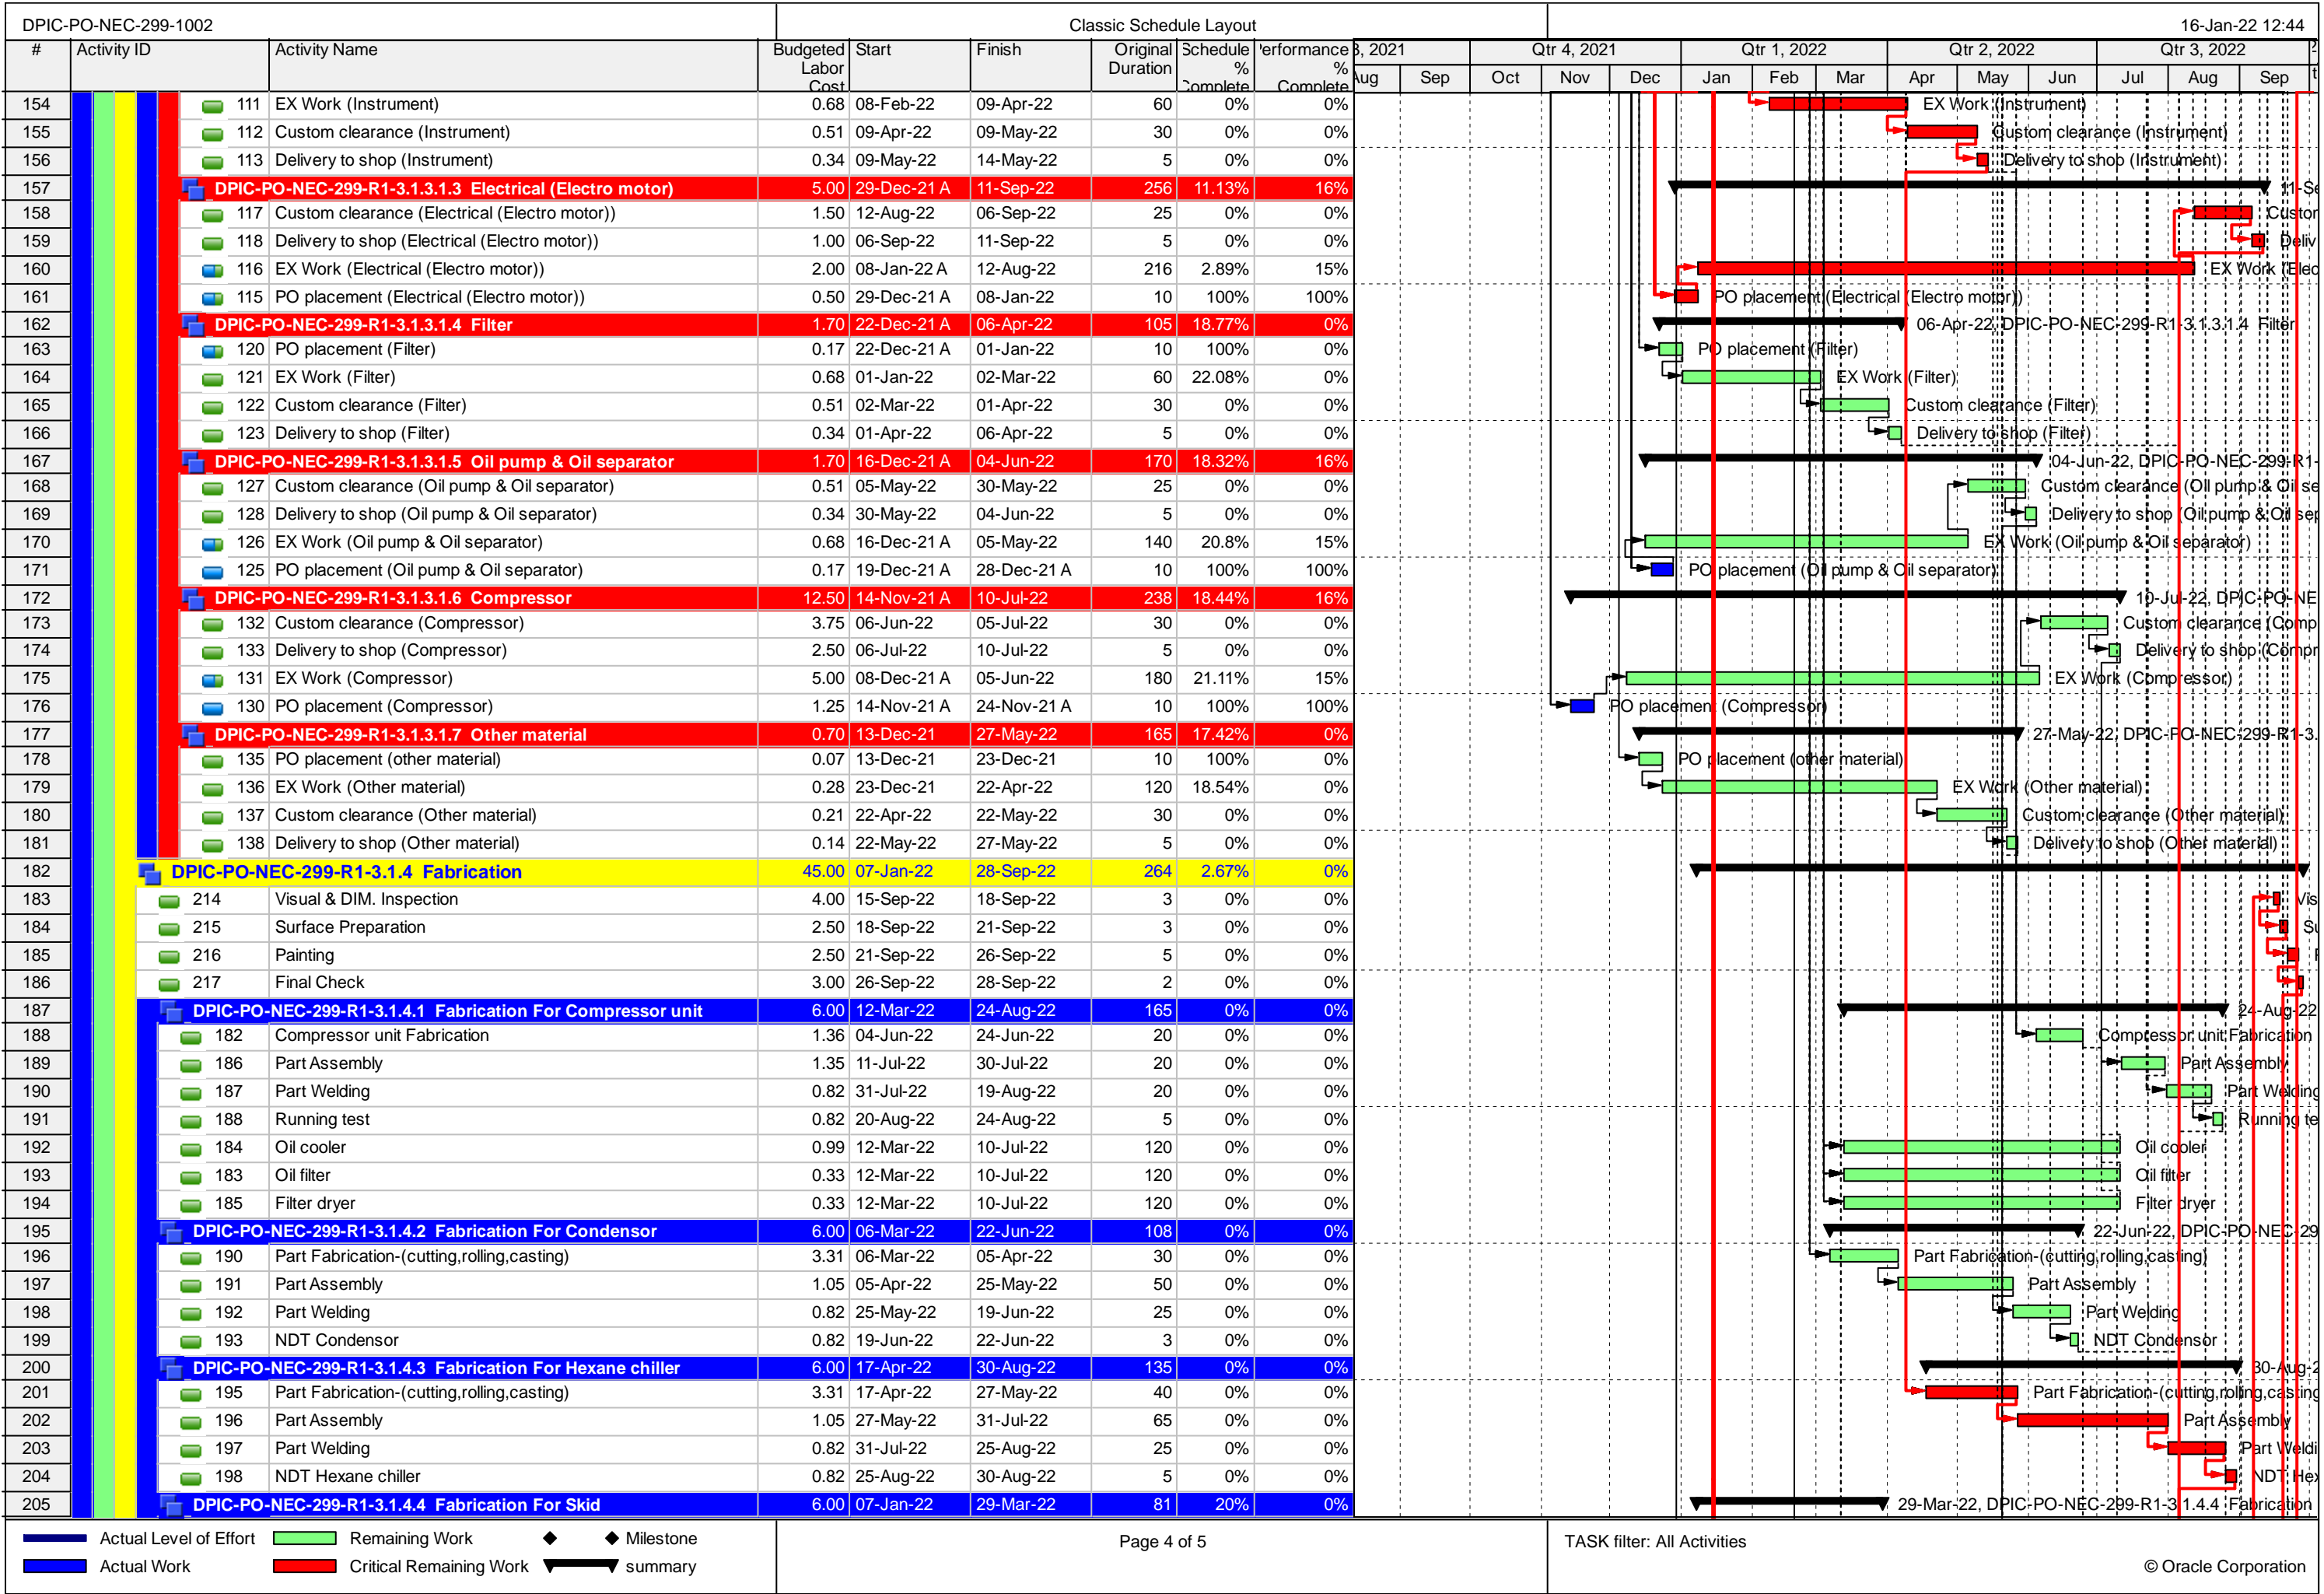









summary

Page 3 of 5

TASK filter: All Activities

© Oracle Corporation



DPIC-PO-NEC-299-1002				Classic Schedule Layout					16-Jan-22 12:44														
#	Activity ID	Activity Name	Budgeted Labor Cost	Start	Finish	Original Duration	Schedule % Complete	Performance % Complete	Qtr 4, 2021		Qtr 1, 2022		Qtr 2, 2022			Qtr 3, 2022							
									Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	
206		 200 Part Fabrication-(cutting,rolling,casting)	3.31	07-Jan-22	27-Jan-22	20	36.25%	0%															
207		 201 Part Assembly	1.05	27-Jan-22	16-Feb-22	20	0%	0%															
208		 202 Part Welding	0.82	28-Feb-22	19-Mar-22	20	0%	0%															
209		 203 NDT Skid	0.82	20-Mar-22	29-Mar-22	10	0%	0%															
210		 DPIC-PO-NEC-299-R1-3.1.4.5 Fabrication For Other	3.00	29-May-22	23-Jul-22	55	0%	0%															
211		 205 Part Fabrication-(cutting,rolling,casting)	1.75	29-May-22	18-Jun-22	20	0%	0%															
212		 206 Part Assembly	0.75	18-Jun-22	03-Jul-22	15	0%	0%															
213		 207 Part Welding	0.25	03-Jul-22	18-Jul-22	15	0%	0%															
214		 208 Hydro test	0.25	18-Jul-22	23-Jul-22	5	0%	0%															
215		 DPIC-PO-NEC-299-R1-3.1.4.6 Assembly of packages on skid	6.00	14-Aug-22	15-Sep-22	32	0%	0%															
216		 210 Inter connecting piping	3.31	14-Aug-22	29-Aug-22	15	0%	0%															
217		 211 Part Assembly	1.05	29-Aug-22	03-Sep-22	5	0%	0%															
218	 212 Part Welding	0.82	03-Sep-22	10-Sep-22	7	0%	0%																
219	 213 NDT packages on skid	0.82	10-Sep-22	15-Sep-22	5	0%	0%																
220	 DPIC-PO-NEC-299-R1-3.1.5 FINAL INSPECTION TEST and RELEASE NOTE for Ex-Work	10.00	28-Sep-22	30-Sep-22	2	0%	0%																
221	 219 FINAL INSPECTION TEST and RELEASE NOTE for Ex-Work	10.00	28-Sep-22	30-Sep-22	2	0%	0%																
222	 DPIC-PO-NEC-299-R1-3.1.6 Final Data Book	5.00	30-Sep-22	04-Oct-22	4	0%	0%																
223	 221 VENDOR FINAL DATA BOOK	5.00	30-Sep-22	04-Oct-22	4	0%	0%																

Page 5 of 5

TASK filter: All Activities

© Oracle Corporation
